Dull Report - APACHE - JUNE WEST B-11HJ - 10.625"

ULTERRA

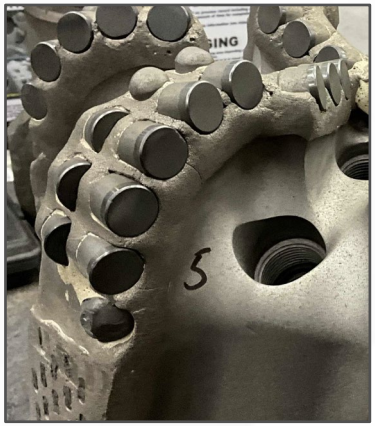

WELL			RIG		STATE - COUNTY		RUN DATE	DIRECTIONAL COMPANY
JUNE WEST B-11HJ			HELMRICH & PAYNE-268		TX-MIDLAND		2025-04-03	BAKER HUGHES
SIZE	**TYPE**	**SERIAL**	**DEPTH IN (ft)**	**DEPTH OUT (ft)**	**DRILLED (ft)**	**HRS**	**ROP (ft/hr)**	**DULL GRADE**
10.625	SPL616	76213	426	6,184	5,758	19.8	292	1-1-ER-A-IN-NO-TD
BHA	BIT, MOTOR, 8"FLOAT SUB, 8"UBHO, 8"NMDC, 10.125"STAB, 8"NMDC, 8"FILTER SUB, XO, 15-8"DC, XO							
COMMENTS					**FORMATION**	JO MILL		
